
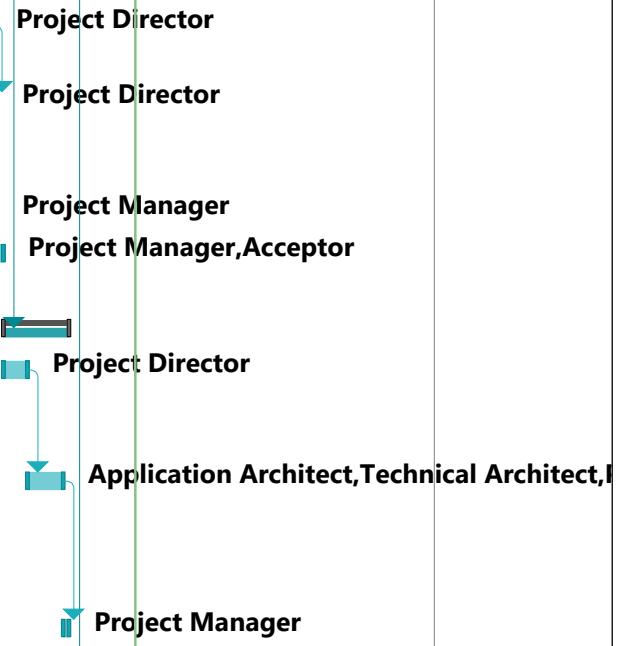



ID		Task Mode	Task Name	Duration	Start	Finish																								
							24	'25 Sep	31	07	14	21	28	'25 Oct	05	12	19	26	'25 Nov	02	09	16	23	'25 Dec	30	07	14			
0			Project Management for MS Website	75 days?	Mon 25-09-08	Fri 25-11-21																								
1			Intiation & Scoping	14 days?	Mon 25-09-08	Sun 25-09-21																								
2			Develop Project Charter & Scope Definition	3 days?	Mon 25-09-08	Wed 25-09-10																								
3			Identify Goals and Objectives	1 day?	Mon 25-09-08	Mon 25-09-08	 Project Director																							
4			Meet with faculty advisor to confirm scope	1 day?	Tue 25-09-09	Tue 25-09-09	 Project Director																							
5			Define constraints	1 day?	Tue 25-09-09	Tue 25-09-09	 Project Manager																							
6			Assign team roles and responsibilities	1 day	Wed 25-09-10	Wed 25-09-10	 Project Manager,Acceptor																							
7			Preliminary Research	11 days	Thu 25-09-11	Sun 25-09-21																								
8			Review inverter topologies and EV power systems	4 days	Thu 25-09-11	Sun 25-09-14	 Project Director																							
9			Study MSI architectures and component optimization	6 days	Mon 25-09-15	Sat 25-09-20	 Application Architect,Technical Architect,...																							
10			Document findings for R1 background section	1 day	Sun 25-09-21	Sun 25-09-21	 Project Manager																							
11			Requirements & Planning	13 days?	Mon 25-09-22	Sat 25-10-04																								

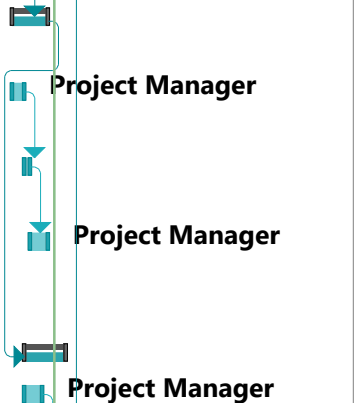


Project: Project Management fo Date: Fri 25-10-03	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	'25 Sep												'25 Oct				'25 Nov				'25 Dec			
							24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14							
12			Stakeholder Requirements & Traceability	6 days	Mon 25-09-22	Sat 25-09-27																								
13				Translate performance needs into engineering specs	2 days	Mon 25-09-22																					Tue 25-09-23			
14				Build traceability matrix	2 days	Wed 25-09-24																					Thu 25-09-25			
15	 			Define acceptance criteria for simulation and prototype	2 days	Fri 25-09-26																					Sat 25-09-27			
16			Design Process Planning	6 days?	Fri 25-09-26	Wed 25-10-01																								
17	 		Map design workflow	2 days	Fri 25-09-26	Sat 25-09-27																								
18			Identify interdependencies	1 day?	Sun 25-09-28	Sun 25-09-28																								
19	 		Plan quality assurance and tracking methods	3 days	Mon 25-09-29	Wed 25-10-01																								
20			Use Case Development	7 days	Sun 25-09-28	Sat 25-10-04																								
21	 		Define EV operating scenarios	3 days	Sun 25-09-28	Tue 25-09-30																								

Project: Project Management for Date: Fri 25-10-03	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


ID	 Task Mode	Task Name	Duration	Start	Finish	'25 Sep 24 31 07 14 21 '25 Oct 28 05 12 19 26 '25 Nov 02 09 16 23 '25 Dec 30 07 14													
22	  	Create use cases for inverter behavior under different loads	4 days	Wed 25-10-01	Sat 25-10-04										 Project Manager				
23	 	Simulation & R1 Report	6 days?	Sun 25-10-05	Fri 25-10-10														
24	 	PSIM Simulation Setup	5 days	Sun 25-10-05	Thu 25-10-09														
25	 	Design initial MSI topology in PSIM	4 days	Sun 25-10-05	Wed 25-10-08										 Project Director				
26	 	Run baseline simulations for voltage/current behavior	1 day	Thu 25-10-09	Thu 25-10-09										 Project Director				
27		Analyze Switching Losses and Controllability	3 days	Tue 25-10-07	Thu 25-10-09														
28	 	Evaluate switching losses	3 days	Tue 25-10-07	Thu 25-10-09														
29	 	Assess controllability across performance range	3 days	Tue 25-10-07	Thu 25-10-09														
30	 	R1 Report Finalization	3 days?	Tue 25-10-07	Fri 25-10-10														
31	 	Compile all sections	2 days	Wed 25-10-08	Thu 25-10-09										 Project Manager				
32	  	Complete contribution matrix	1 day	Fri 25-10-10	Fri 25-10-10										 Project Manager				
33	  	Submission	1 day?	Fri 25-10-10	Fri 25-10-10										 Project Manager				

Project: Project Management fo Date: Fri 25-10-03		Task		Inactive Summary		External Tasks	
		Split		Manual Task		External Milestone	
		Milestone		Duration-only		Deadline	
		Summary		Manual Summary Rollup		Progress	
		Project Summary		Manual Summary		Manual Progress	
		Inactive Task		Start-only			
		Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish								'25 Sep				'25 Oct				'25 Nov				'25 Dec																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
							24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
34			Conceptual Design & R2 Report	22 days?	Fri 25-10-10	Fri 25-10-31																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									</

Project: Project Management for Date: Fri 25-10-03	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	'25 Sep					'25 Oct					'25 Nov				'25 Dec																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
							24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
44			Define integration tests for simulation-to-hardware transition	6 days	Wed 25-10-22	Mon 25-10-27																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

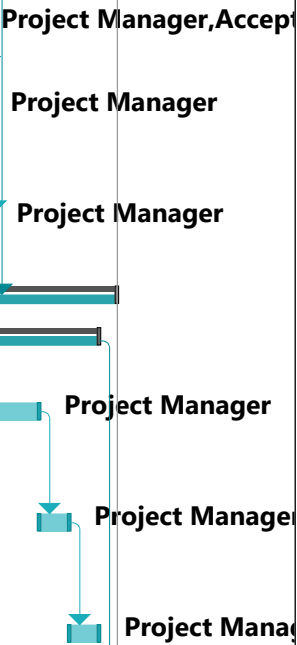

Project: Project Management for

Date: Fri 25-10-03

Task

Split


Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress











ID		Task Mode	Task Name	Duration	Start	Finish	'25 Sep					'25 Oct				'25 Nov				'25 Dec			
							24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14
55			Final Presentation & Demo	3 days?	Wed 25-11-19	Fri 25-11-21																	
56			Prepare slides and demo script	1 day?	Wed 25-11-19	Wed 25-11-19																	
57			Rehearse team presentation	1 day?	Thu 25-11-20	Thu 25-11-20																	
58			Finalization & Present	1 day?	Fri 25-11-21	Fri 25-11-21																	

Contracts M

Project: Project Management fo Date: Fri 25-10-03	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
